

## STATE OF TENNESSEE DEPARTMENT OF ENVIRONMENT AND CONSERVATION NASHVILLE ENVIRONMENTAL FIELD OFFICE DIVISION OF WATER RESOURCES 711 R.S. GASS BOULEVARD NASHVILLE, TN 37243 PHONE 615-687-7000 STATEWIDE 1-888-891-8332 FAX 615-687-7078

June 8, 2020

Tarun Surti 5928 Westheimer Drive Brentwood, TN 37204 ecopy: <u>tarunsurti@comcast.net</u>

Subject: Notice of Violation Aloft Hotels 608 McGavock Pike Nashville, Davidson County, TN TNR240679

Dear Mr. Surti:

On June 4, 2020, the Division of Water Resources (the Division) made a compliance evaluation inspection (CEI) at the Aloft Hotel construction site located at 608 McGavock Pike Davidson County, Nashville, TN. During the inspection, Division staff inspected the site's stormwater pollution prevention plan (SWPPP), erosion prevention sediment controls (EPSCs), inspection reports and best management practices (BMPs) for compliance with the Construction General Permit (CGP).

During the CEI, the Division found the following violations:

- 1) EPSC's were missing on the north end of the site protecting the water feature from the disturbed area;
- The inspector for the site performing the required twice weekly inspections was listed as John Dennis. There is no record that Mr. Dennis has a valid certification from the "Fundamentals of Erosion Prevention and Sediment Control Level I" course as required by CGP Section 3.5.8.1(a);

Mr. Tarun Surti June 8, 2020 Page **2** of **2** 

3) The SWPP for the site identified a wetlands buffer to the south. Construction was observed in this area, but it could not be determined during the site inspection if the wetlands buffer has been violated.

In order to begin bringing this site into compliance, you must complete the following by **June 22, 2020**:

- 1) Install EPSCs along the north end of the site to protect the water feature and provide photo documentation;
- 2) Provide documentation that the inspector of the site has completed the "Fundamentals of Erosion Prevention and Sediment Control Level I or meets the other requirements listed in Section 3.5.8.1 in the CGP;
- 3) Provide a site plan showing the extent of the disturbance in the south end of the property in relation to the required wetlands buffer. The plan must be certified by Tennessee Professional Engineer.

Note that the site has coverage under ARAP NRS16.124. There are possible violations as well under this permit, so documentation has been sent to the permit writer for further evaluation.

Your prompt attention to these matters is greatly appreciated. If you have any questions regarding this matter, please contact me at 615-687-7106 or John.Leffew@tn.gov.

Sincerely,

ohn w. Leffen

John W. Leffew, P.G. Division of Water Resources

Cc:

Bill Murph, TDEC-DWR, <u>Bill.Murph@tn.gov</u> Tim Jennette, TDEC-DWR, <u>Tim.Jennette@tn.gov</u> Michael Hunt, Metro Water Services, <u>Michael.Hunt@nashville.gov</u> James Edwards, Superintendent, JAFielden, <u>jamese@jafielden.com</u> Joshua Dennis, Assistant Superintendent, <u>joshuad@jafielden.com</u>

Attachment



## TENNESSEE DEPARTMENT OF ENVIRONMENT AND CONSERVATION

Division of Water Resources

William R. Snodgrass Tennessee Tower, 312 Rosa L. Parks Avenue, 11th Floor, Nashville TN 37243

1-888-891-8332 (TDEC)

## Compliance Inspection for General NPDES Permit for Stormwater Discharges from Construction Activities (CGP)

						NPDES Tracking Number:				TNR240679
Site/Project Name:	Aloft Hotel				Date Coverage was Issued:				26-Oct-16	
	608 McGavock Pike					Start Date:				1-Aug-16
Street Address or		Estim	ated	End	Date:	31-Dec-17				
Location:		Latitu	Jde (	dd.d	ddd):	36.1547				
Site Description:		Longi	tude	(-dd	.dddd):	-86.6825				
Description:				-indiction: TNC0C0047		Acres Disturbed:			d:	3.8
County(ies): Davidson EFO: Nashville M			MS4 Ju	4 Jurisdiction: TNS068047			Acre	<b>S:</b>		
Name of Permittee (Developer/Operator):    608 Hotels, LLC      Contact Phone: 615-812-										
Name of Official Contact: Tarun Surti				Email: tarunsurti@comcast.net					6164	
Address: 5928 Westheimer Drive				City: Brentwood					State: TN	<b>Zip:</b> 37204
Construction Phase: Site preparation Grading Construction Final Stabilization										
Inspection Purpose:	V	Routine Foll	ow-up [	Complaint NO	1		Maa	N		omments
					ant a bili-	hoda	Yes			
Have all construction activities stopped and 70% uniform permanent cover established:										mmonte
							Yes	N		omments
Notable impacts to waters as a result of site activities/discharges?								┼╞═		
Evidence of insufficiently treated stormwater discharges at outfall locations?								┼┝═	<u> </u>	
Evidence of structural EPSC measure failure/absence?										
Evidence of non-structural EPSC measure failure/absence?										
Unauthorized discharges?							H	╆┝	╡┼	
Evidence of offsite impacts?									ARAP	
Evidence of construction buffer disturbance?  Image: ARAP    Compliance Evaluation: Any Y = recommend NOV/EAR or follow-up - date:										
Compliance Evaluation: A	'ny	Y = recommend N	OV/EAR	( email, letter, inspec	tion, et	c.) - dat	e:			
/	Any	Y = recommend i	ollow-up	(email, letter, inspec			Yes	N	C	omments
			the set of the		7		P		1	
Are copies of the SWPPP & inspection reports on site or made available?							H		1	
Has SWPPP been implemented & satisfactory?							H	۲ř	╡┼────	
Are 2/week inspections being performed?							H	┼╞═		
Are inspection reports completed & signed?							R	┼╞═		
Are inspection reports filled out by a qualified EPSC inspector?								-	JOLD DE	inn is
Compliance Evaluation: A	ny	N = recommend f	ollow-up	(email, letter, inspect	tion, etc	.) date:		-		
							Yes	No		omments
Are there ARAP violations	sor	unauthorized stre	eam/wetl	and alteration?			5		NR 16.	124
Compliance Evaluation: Y	' = p	erform follow-up	ARAP ins	spection - date:						
Notes: See Pare	Q.									
On-Site Contact (if availabl			M							
On-Site Contact Name (Pri	nt):	On-Site Co	ontact Titl	le:	Signa	ature:				Date:
	_								FO: Nashville	FEO
TDEC Personnel/Informatio	DN	T	1	1100	Date	: 6/4/	1010			Sass Boulevard
Inspector's Name (Print):		Signature	: Color	w. Juli		: 120		-		TN 37216
John W. Leffer			1	11/1	Interior	a / 100	~		······	

CN-1067 (Rev. 26MAR19)

EPSC measures missing on N side of site along water feature. Sediment observed leaving the site through the N side where the EPSC's are missing. A rain event just occurred Prior to the inspection. Water in the channel was very turbid and brown, but the Same conditions were observed upstream. work on ARAP NRS 16.124 was in Process. Wetlands area to the South

may have been violated.



Photo 1: View of site from Lakeland Dr. looking west.



Photo 2: View of ARAP NRS16.124 construction area.



Photo 3: View of NRS16.124 construction area.



Photo 4: View of ARAP NRS16.124 construction area looking south.



Photo 5: View of ARAP NRS16.124 construction area.



Photo 6: North end of site. Note that the feature is not protected from the disturbed area by EPSCs



Photo 7: View of feature looking south.



Photo 8: View of south end of site. Wetlands buffer is in this area.

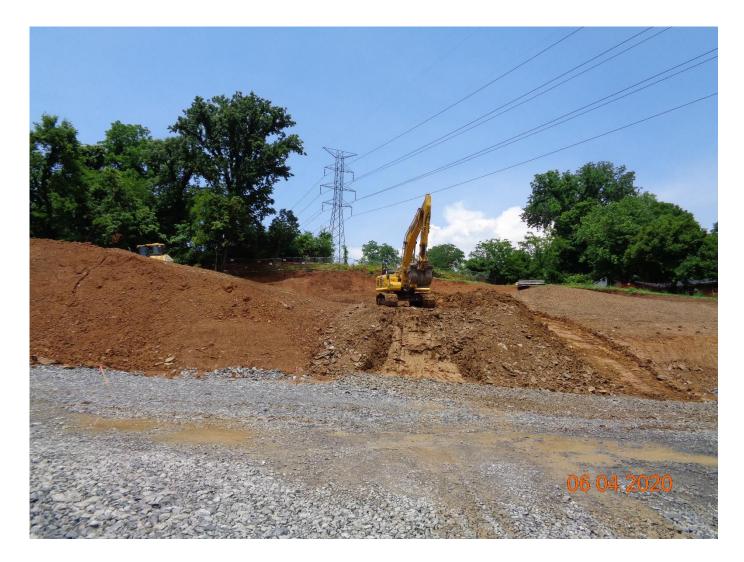


Photo 9: View looking west.
